ID	Task Name
1	**ASN Africa-Europe Baseline System - Melkbosstrand PiP Programme**
2	
3	
4	Contract Award
5	**Initial Delay (Lack of Technical Information)**
6	Commencement
7	
8	**Project Management**
9	Fortnightly Reporting
10	Ongoing Communication
11	Quality and Financial Control
12	Permit Book
13	Close Out Book
14	
15	**Delay**
16	
17	**Screening**
18	Desktop Review
19	Pre-application meeting with DEA
20	Site Visit
21	Reporting and Sign-off
22	Screening Complete
23	
24	**Specialist Studies**
25	Drafting Terms of Reference by ACER
26	ASN Review
27	ACER Finalization
28	Obtain Specialist Proposals and Budgets
29	Commission Specialists
30	Site Visits
31	Specialist Investigations
32	Specialist Reporting
33	Draft Specialist Reports Submission
34	ACER Review
35	ASN Review
36	Specialists Revisions and Submission to ACER
37	Specialist Studies Complete
38	
39	**Project Announcement**
40	Prepare Adverts, BID, Letters, etc
41	ASN Review
42	ACER Finalization
43	Printing
44	Announcement Period
45	Public Comment Period
46	Public Open Day (x 1)
47	Issues and Responses Report
48	Project Announcement Complete
49	
50	**Draft Scoping Report (DSR)**
51	Drafting of DSR by ACER
52	ASN Review
53	ACER Finalization
54	DSR Complete
55	
56	**Draft Environmental Impact Assessment Report (DEIAR) - Initial**
57	Drafting of DEIAR and EMPr by ACER
58	DEIAR and EMPr Complete (As far as possible)
59	
60	**Application for Environmental Authorization**
61	Delays in signing of old DEA application
62	Delays in signing the updated DEA Application
63	Drafting by ACER
64	ASN Review
65	ACER Finalization
66	Application Complete for Submission
67	Submit Application and Draft Scoping Report to DEA
68	DEA Acknowledgement of Application
69	Application Complete
70	
71	**DSR Public Review**
72	Prepare Announcement Material
73	ASN Review
74	ACER Finalization

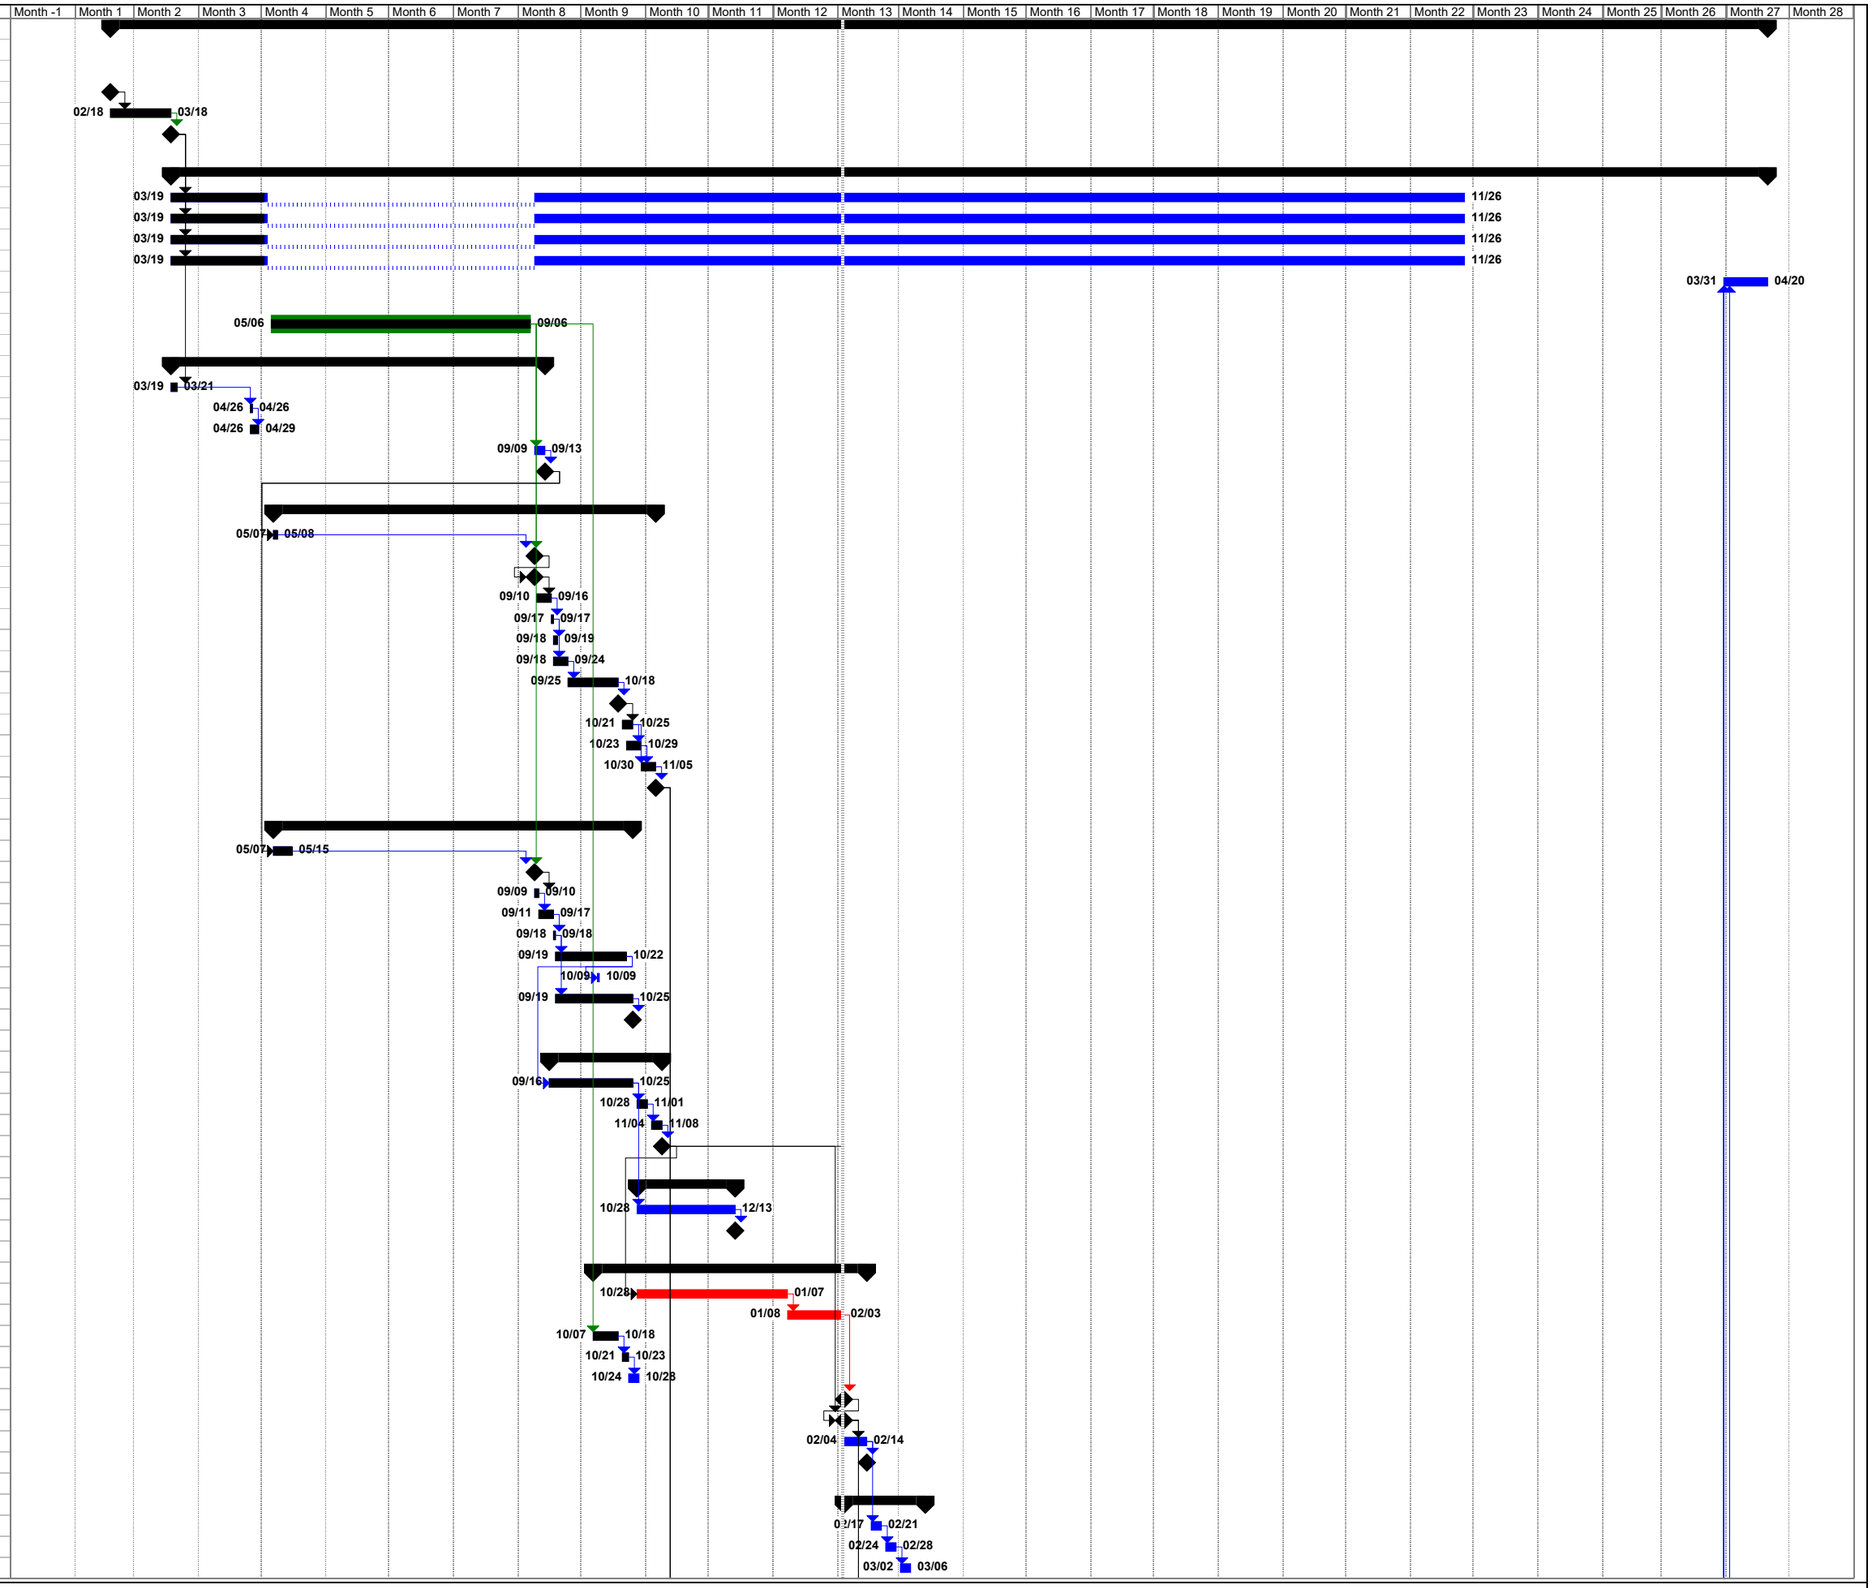

ASN - Africa-Europe Baseline System
16 Jan 2020

Task | Milestone | Rolled Up Task | Rolled Up Progress | External Tasks | Group By Summary
Progress | Summary | Rolled Up Milestone | Split | Project Summary | Deadline

ID	Task Name
75	Announcement Period
76	Public Review Period
77	Public Open Day (x 1)
78	Issues and Responses Report
79	Authority consultation
80	DSR Public Review Complete
81	
82	**Final Scoping Report (FSR)**
83	ACER Amendments to DSR
84	ASN Review
85	ACER Finalization
86	Submit FSR and Issues and Response Report to DEA
87	DEA Acknowledgement
88	Letters to I&APs re FSR (and where it can be accessed)
89	DEA Feedback on FSR
90	FSR Complete
91	
92	**Draft Environmental Impact Assessment Report (DEIAR) - Completion**
93	Specialist Revisions (If Required)
94	Final Drafting of DEIAR and EMPr by ACER
95	ASN Review
96	ACER Finalization
97	DEIAR and EMPr Complete
98	
99	**DEA Compulsory Shut Down Period (Public Participation)**
100	
101	**DEIAR and EMPr Public Review**
102	Prepare Announcement Material
103	ASN Review
104	ACER Finalization
105	Announcement Period
106	Public Review Period
107	Public Open Day (x 1)
108	Issues and Responses Report
109	Authority consultation
110	DEIAR and EMPr Public Review Complete
111	
112	**Final Environmental Impact Assessment Report (FEIAR)**
113	ACER Amendments to DEIAR and EMPr
114	Issues and Response Report
115	ASN Review
116	ACER Finalization
117	Submit FEIAR, EMPr and Issues and Response Report to DEA
118	DEA Acknowledgement
119	Letters to I&APs re FEIAR and EMPr (and where they can be accessed)
120	
121	**EIA Complete (Awaiting Environmental Authorization)**
122	Environmental authorisation issued by DEA
123	EIA complete
124	
125	**Associated Permits and Licenses**
126	Heritage Permit
127	Protected Plant and Tree Permits
128	Water Use License
129	Seashore Lease Permit
130	Municipal Permits (Coastal Public Property)
131	Beach Driving Permit
132	Authority consultations

ASN - Africa-Europe Baseline System
16 Jan 2020

Task | Milestone | Rolled Up Task | Rolled Up Progress | External Tasks | Group By Summary
Progress | Summary | Rolled Up Milestone | Split | Project Summary | Deadline
