ID	Task Name
1	**ASN Africa-Europe Baseline System - Melkbosstrand PiP Programme**
2	
3	
4	Contract Award
5	**Initial Delay (Lack of Technical Information)**
6	Commencement
7	
8	**Project Management**
9	Fortnightly Reporting
10	Ongoing Communication
11	Quality and Financial Control
12	Permit Book
13	Close Out Book
14	
15	**Delay**
16	
17	**Screening**
18	Desktop Review
19	Pre-application meeting with DEA
20	Site Visit
21	Reporting and Sign-off
22	Screening Complete
23	
24	**Specialist Studies**
25	Drafting Terms of Reference by ACER
26	ASN Review
27	ACER Finalization
28	Obtain Specialist Proposals and Budgets
29	Commission Specialists
30	Site Visits
31	Specialist Investigations
32	Specialist Reporting
33	Draft Specialist Reports Submission
34	ACER Review
35	ASN Review
36	Specialists Revisions and Submission to ACER
37	Specialist Studies Complete
38	
39	**Project Announcement**
40	Prepare Adverts, BID, Letters, etc
41	ASN Review
42	ACER Finalization
43	Printing
44	Announcement Period
45	Public Comment Period
46	Public Open Day (x 1)
47	Issues and Responses Report
48	Project Announcement Complete
49	
50	**Draft Scoping Report (DSR)**
51	Drafting of DSR by ACER
52	ASN Review
53	ACER Finalization
54	DSR Complete
55	
56	**Draft Environmental Impact Assessment Report (DEIAR) - Initial**
57	Drafting of DEIAR and EMPr by ACER
58	DEIAR and EMPr Complete (As far as possible)
59	
60	**Application for Environmental Authorization**
61	Delays in signing of old DEA application
62	Delays in signing the updated DEA Application
63	Drafting by ACER
64	ASN Review
65	ACER Finalization
66	Application Complete for Submission
67	Submit Application and Draft Scoping Report to DEA
68	DEA Acknowledgement of Application
69	Application Complete
70	

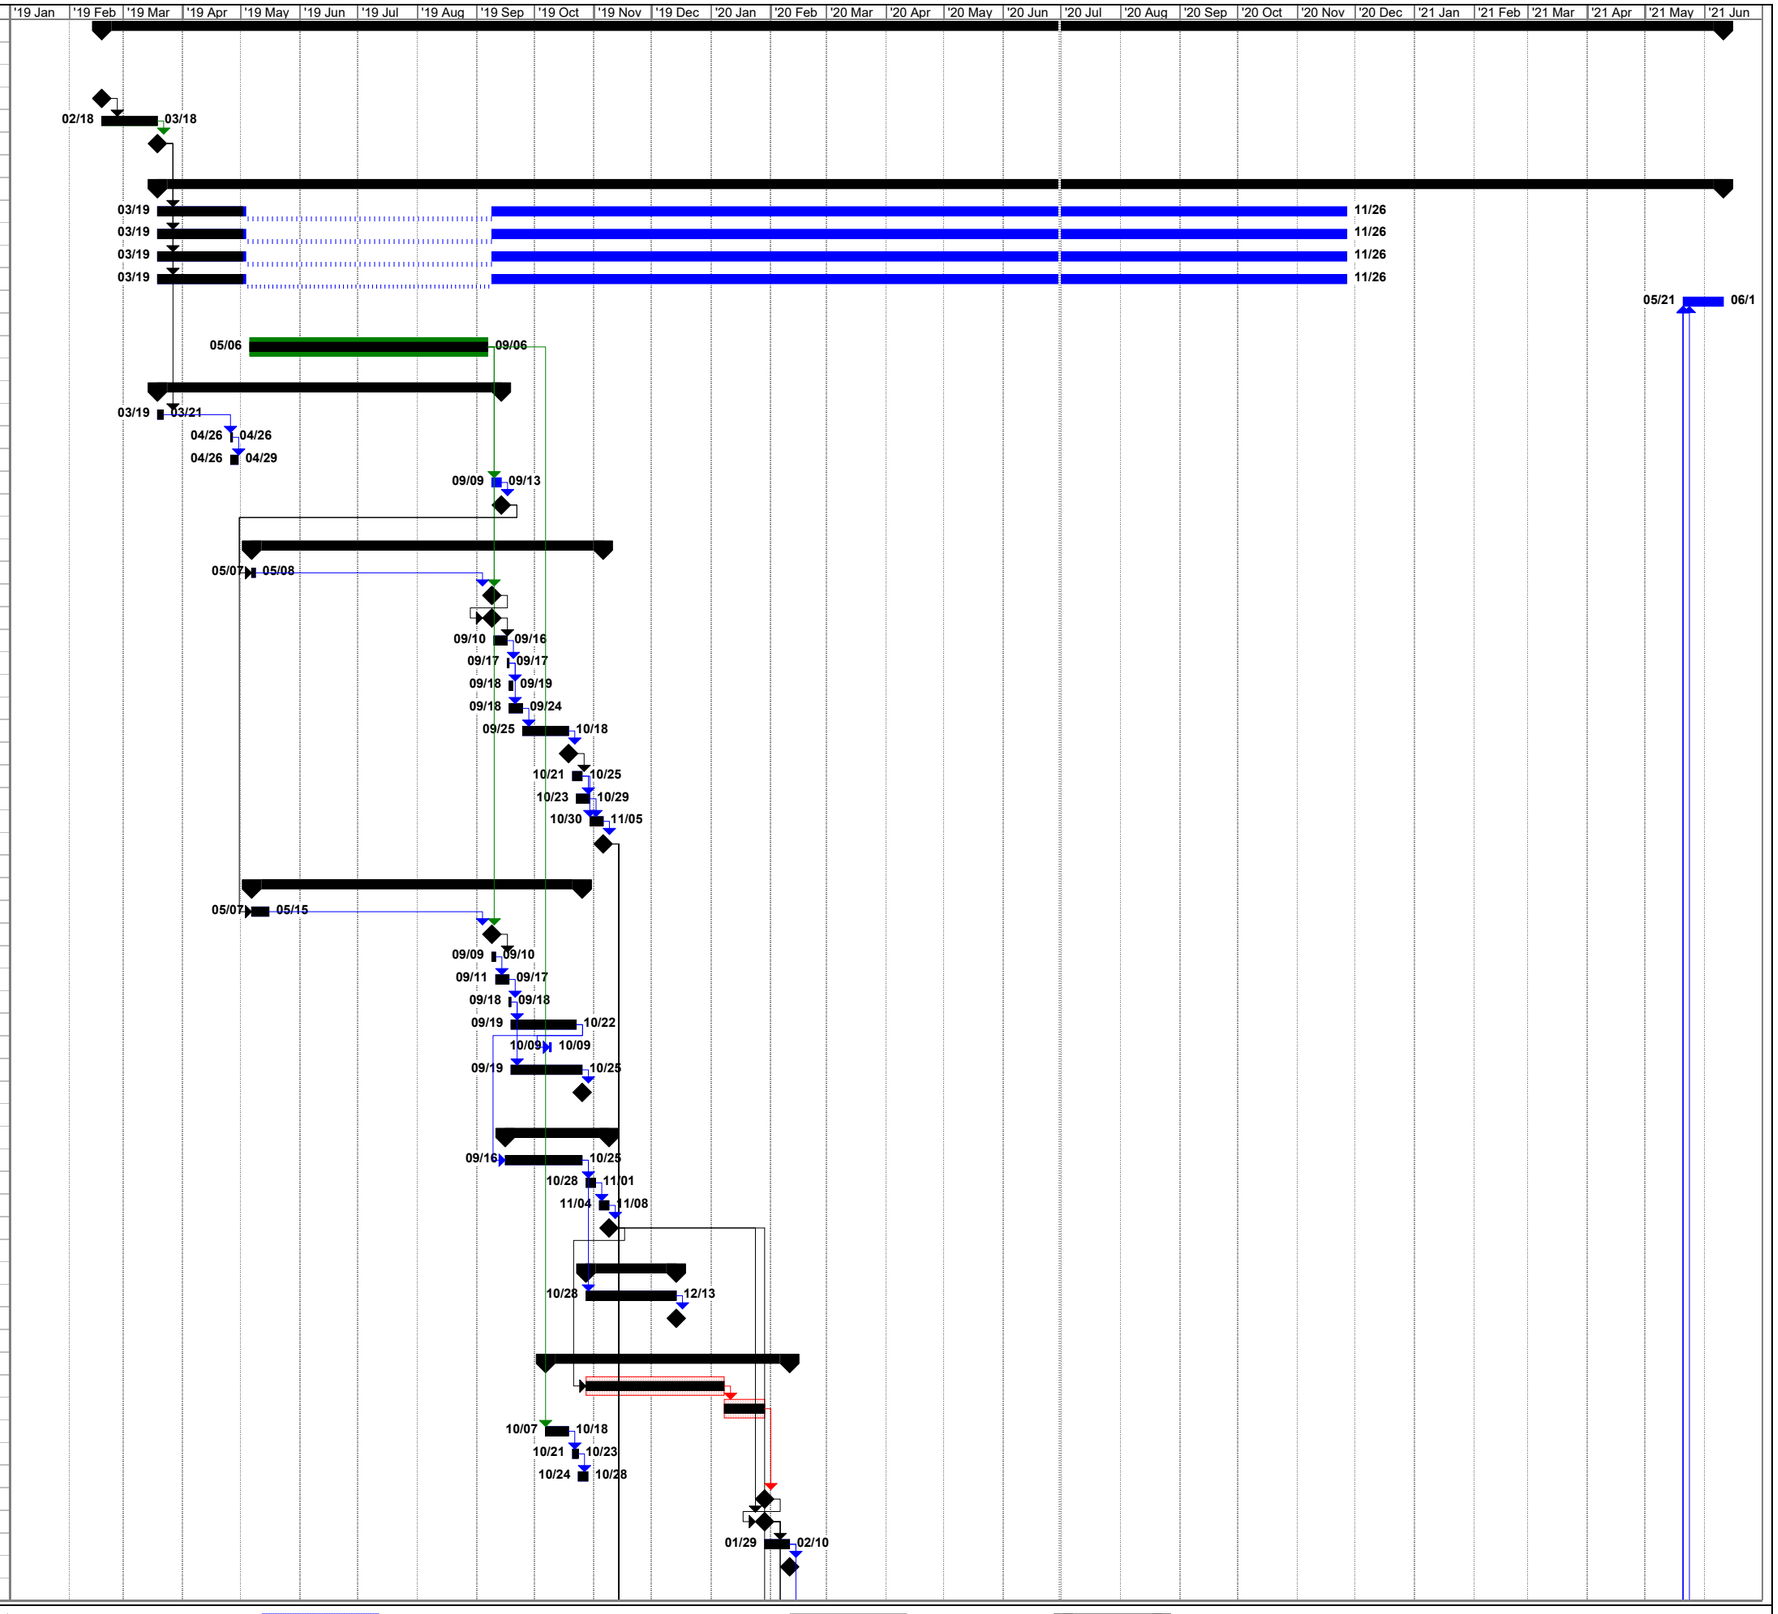

Equiano - Melkbosstrand
Tracking Programme
30 June 2020

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary | Deadline

ID	Task Name
71	**DSR Public Review**
72	Prepare Announcement Material
73	ASN Review
74	ACER Finalization
75	Announcement Period
76	Public Review Period
77	Public Open Day (x 1)
78	Issues and Responses Report
79	Authority consultation
80	DSR Public Review Complete
81	
82	**Final Scoping Report (FSR)**
83	ACER Amendments to DSR
84	Covid-19 Lock Down delay
85	ASN Review
86	ACER Finalization
87	Submit FSR and Issues and Response Report to DEA
88	DEA Acknowledgement
89	Letters to I&APs re FSR (and where it can be accessed)
90	DEA Feedback on FSR
91	FSR Complete
92	
93	**Draft Environmental Impact Assessment Report (DEIAR) - Completion**
94	Specialist Revisions (If Required)
95	Final Drafting of DEIAR and EMPr by ACER
96	ASN Review
97	ACER Finalization
98	DEIAR and EMPr Complete
99	
100	**DEA Compulsory Shut Down Period (Public Participation)**
101	
102	**DEIAR and EMPr Public Review**
103	Prepare Announcement Material
104	ASN Review
105	ACER Finalization
106	Announcement Period
107	Public Review Period
108	Public Open Day (x 1)
109	Issues and Responses Report
110	Authority consultation
111	DEIAR and EMPr Public Review Complete
112	
113	**Final Environmental Impact Assessment Report (FEIAR)**
114	ACER Amendments to DEIAR and EMPr
115	Issues and Response Report
116	ASN Review
117	ACER Finalization
118	Submit FEIAR, EMPr and Issues and Response Report to DEA
119	DEA Acknowledgement
120	Letters to I&APs re FEIAR and EMPr (and where they can be accessed)
121	
122	**EIA Complete (Awaiting Environmental Authorization)**
123	Environmental authorisation issued by DEA
124	EIA complete
125	
126	**Associated Permits and Licenses**
127	Heritage Permit
128	Protected Plant and Tree Permits
129	Water Use License
130	Seashore Lease Permit
131	Municipal Permits (Coastal Public Property)
132	Beach Driving Permit
133	Authority consultations

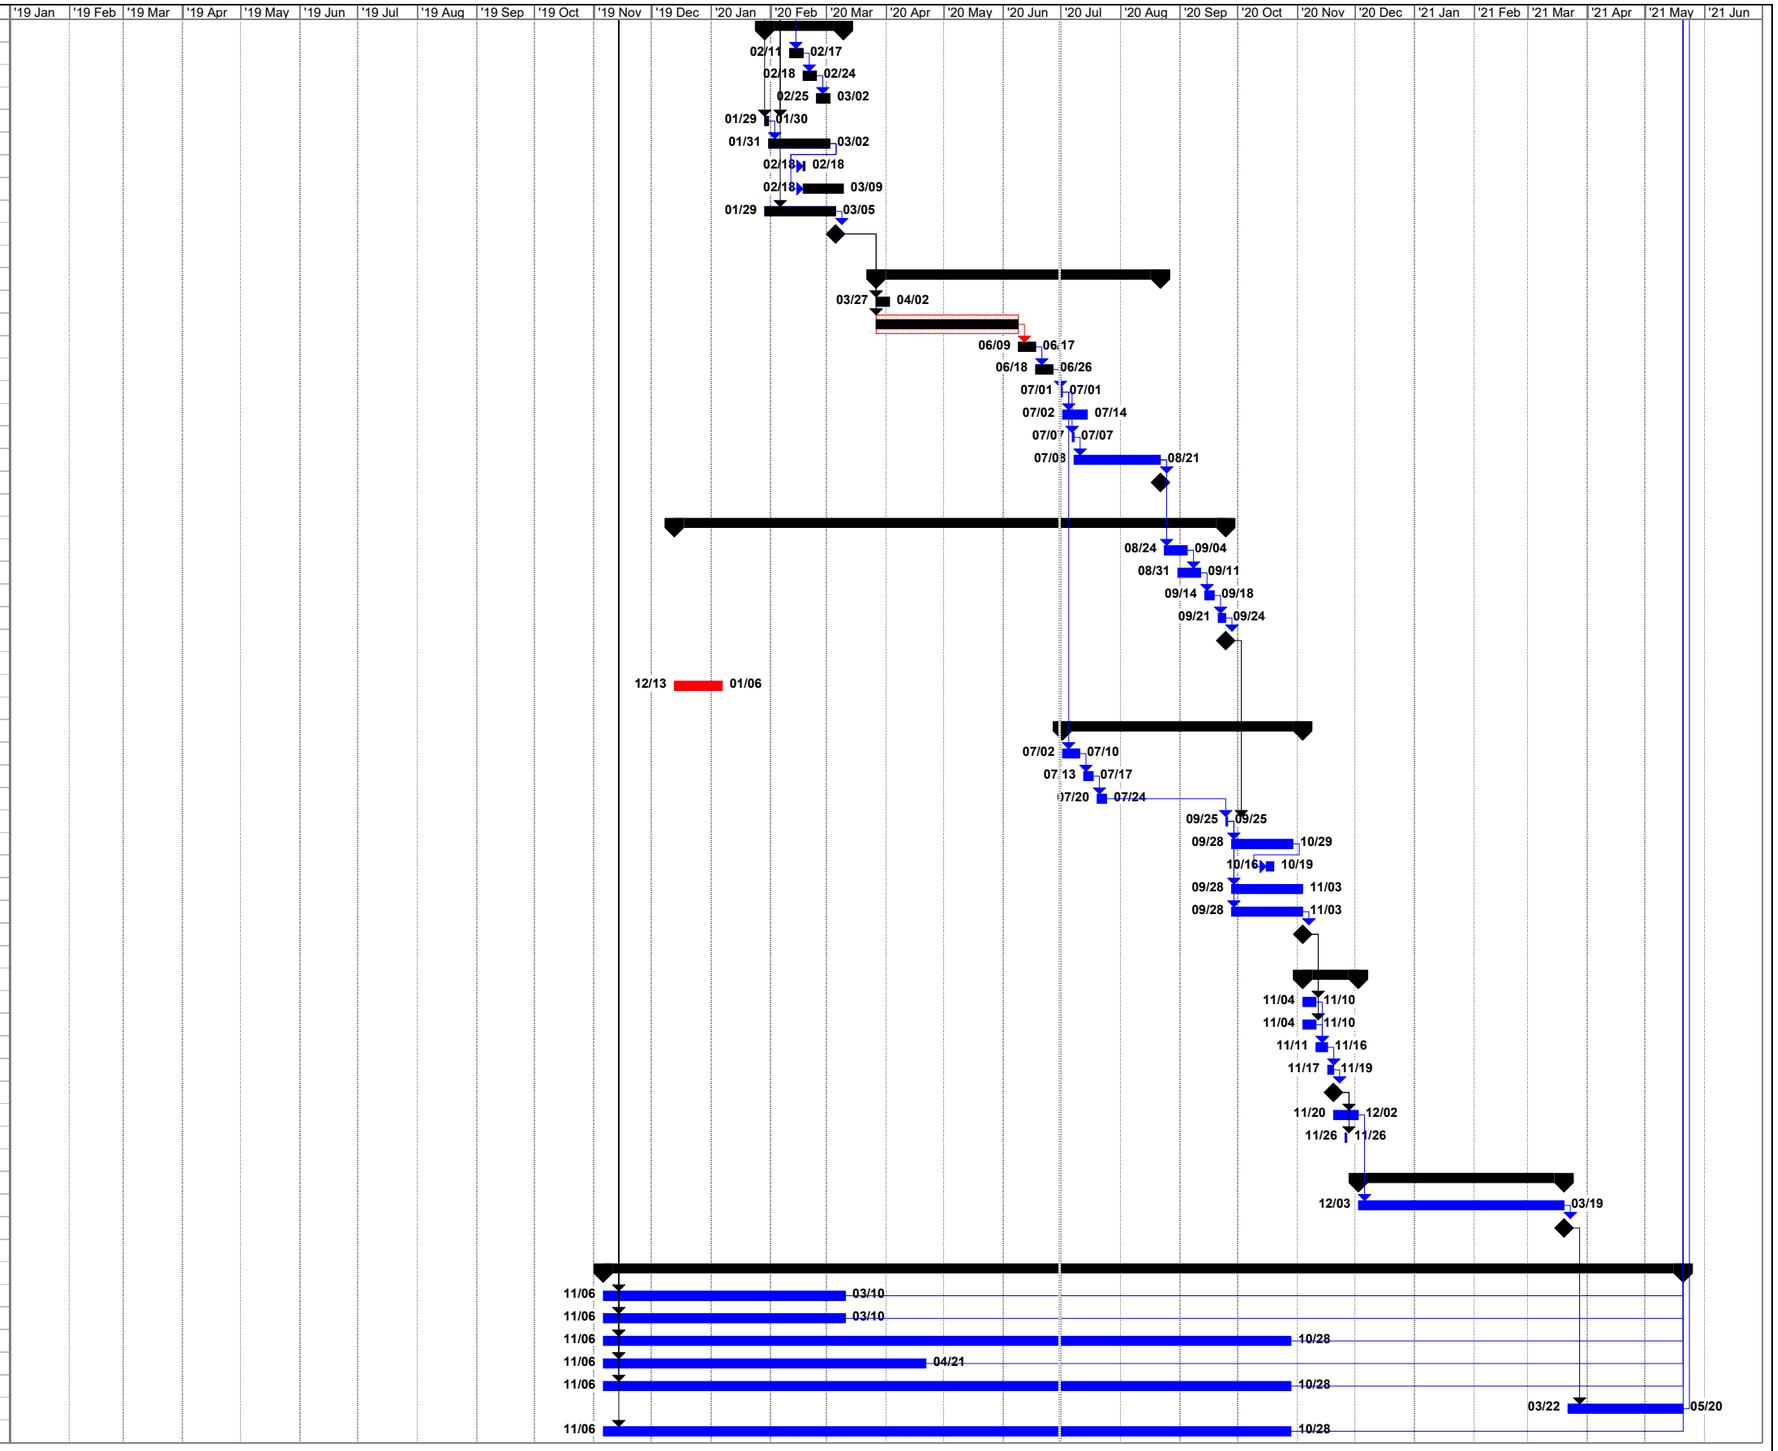

Equiano - Melkbosstrand
Tracking Programme
30 June 2020

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary		Deadline	
